003-MOPR12 · MEETSYNC (ZOOM APP MARKETPLACE)

Product Status Map

What MeetSync is, what is finished, what is not, and the specific reason each unfinished thing is unfinished — drawn rather than described.

Document control

Document	`claude_V001_MoPr12-meetsync_zoom_product_status_map`
Version	V001 · first issue
Date / time	20 Sep 2026, 12:42 BST
Author	Claude for Senthil/KP
Describes	MeetSync code **v0.45.0**; tracker **v040**; external review **Perplexity Review V001** (16 Sep 2026)
Status	Released
Classification	Internal — build and gate evidence
Companion	`claude_V001_MoPr12-meetsync_zoom_versiondetail_manualtest_20260920_*.xlsx`

1 · Context

MeetSync is a Zoom Marketplace app for sales teams. A meeting ends; Zoom produces a transcript; MeetSync reads it, pulls out the commitments and the risk signals, and writes agreed fields into the CRM the customer already uses — under per-field rules the customer sets, with a review step, a queue that survives a crash and an audit row for every write.

The engineering has been unusually disciplined and the product has never been installed by a stranger. Both are true at once, and this document exists so the gap between them is visible at a glance. On 16 September an external reviewer read the code and then checked the claims made *around* it, raising fourteen findings — three of them critical. Code v0.45.0 is the response. The colouring below is the honest state after that response.

2 · How to read these figures

- **Built & reachable** — shipped, customer can invoke it, pinned by a named regression test
- **Built, unverified live** — code complete and tested; never run against the real Zoom or a real CRM
- **Not built** — no code exists
- **Held by a decision** — deliberately not built until Senthil rules

Solid arrows are paths that work today. Dashed red arrows are paths that did not exist before v0.45.0. Every arrow is labelled with what actually moves along it. Each figure makes one claim, stated in its caption.

3 · Figure 1 — The system, coloured by what is actually finished

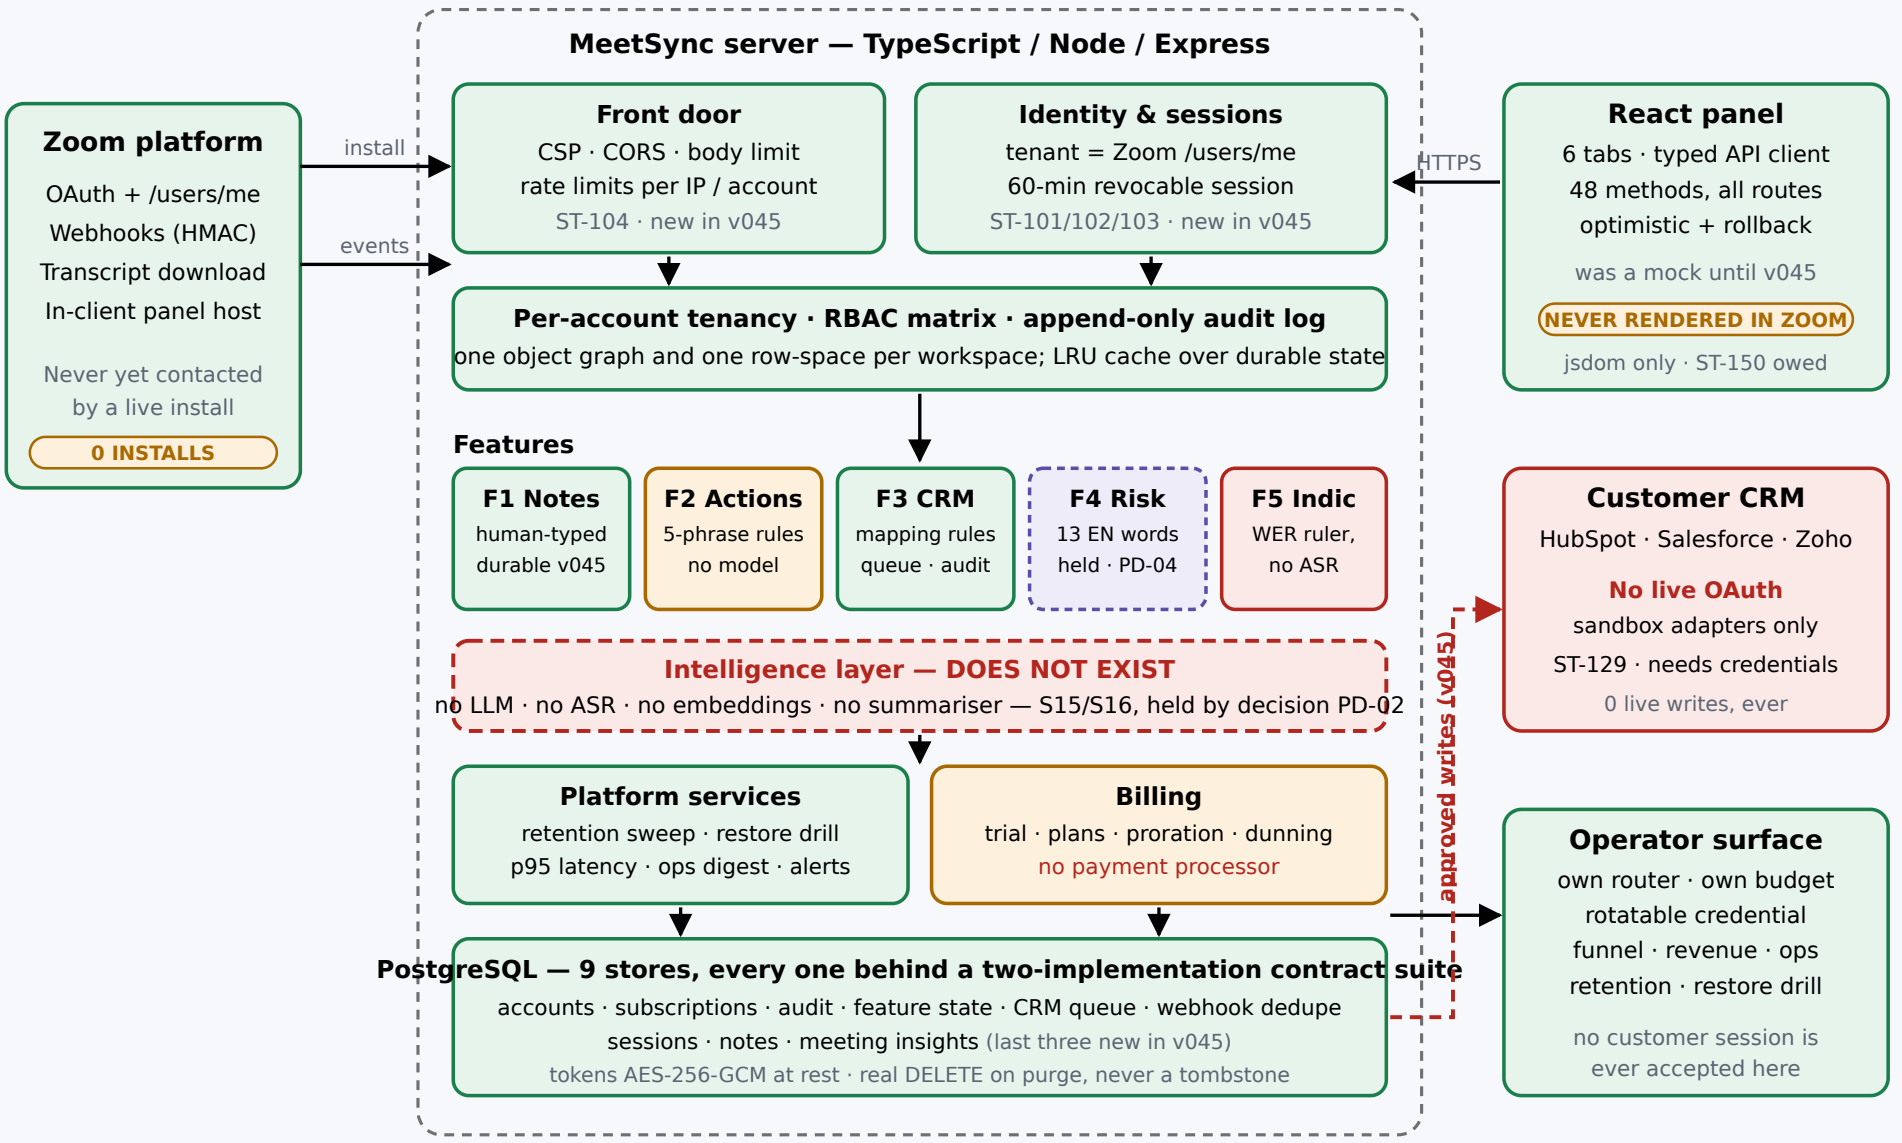


Figure 1. The platform underneath MeetSync is finished and proven; the two things a customer would pay for — real intelligence and a live CRM connection — are the two boxes that are empty. The red dashed path is the writeback route that only began to exist in v0.45.0.

4 · Figure 2 — The install flow: how a stranger could take your workspace, and what stops it now


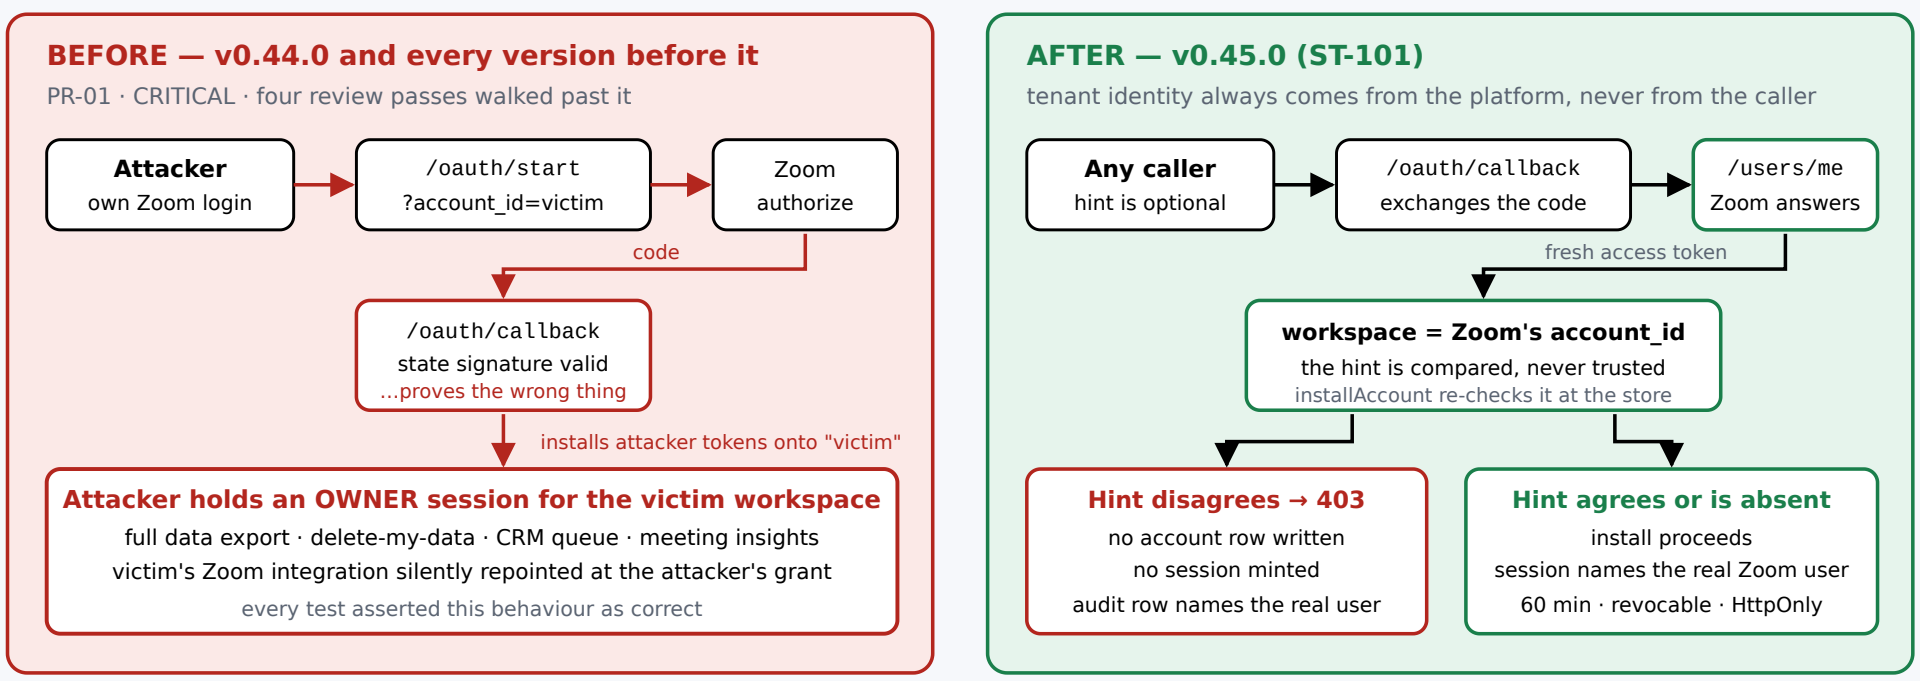


Figure 2. The signature on `state` was never wrong — it proved the server issued that state. It could not prove the caller owned the account, and nothing else asked. One call to `/users/me` is the whole difference between the left panel and the right.

5 · Figure 3 — The product loop, and the two hops that were missing

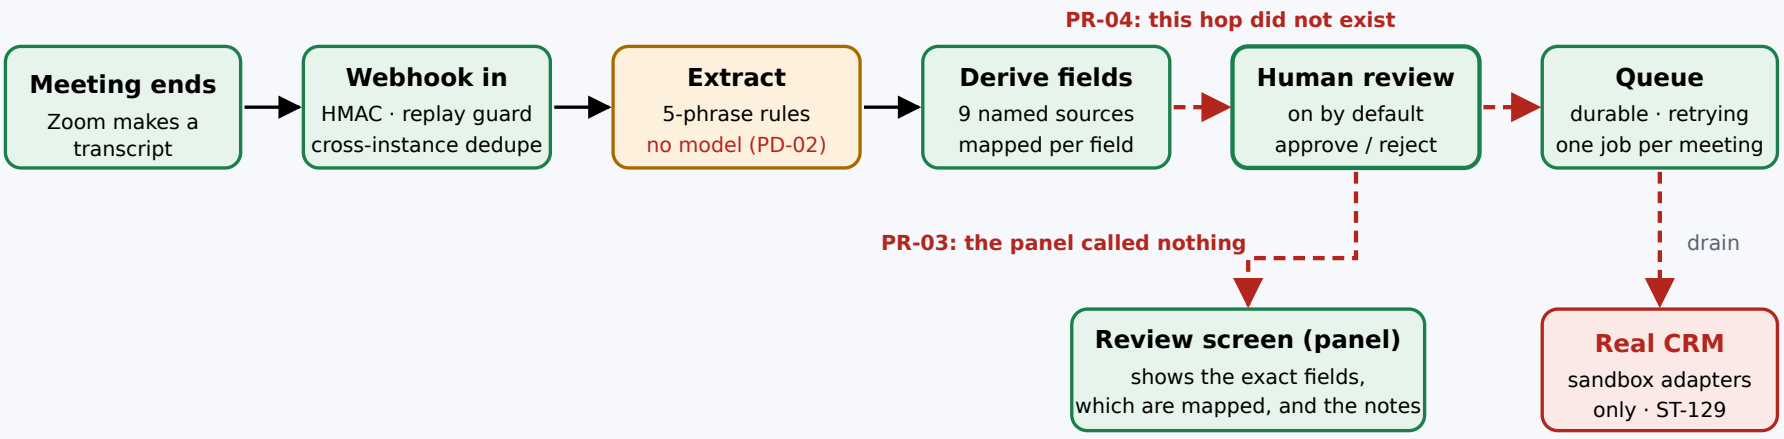

Before v0.45.0 the loop stopped at "derive fields" and a human had to type them into an API call by hand.

Figure 3. Every box on the top row already existed in v0.44.0; of the seven arrows, only the three solid ones did. The product's headline promise — a meeting becomes CRM fields — needed a person to make an API call with fields they had typed themselves.

6 · Figure 4 — Twenty sprints: what is finished, and what each unfinished one is waiting on

Sprint	Points complete	Points	Status	What it is waiting on
S1–S8		248 / 281	Built & tested	Nothing — but never run live
S9		5 / 30	Marketplace prep	Zoom dev app · Handover #2
S10		7 / 24	Docs & remediation	Marketplace approval
S11–S12		6 / 10	Launch & iterate	Real installs · real users
Below: the plan the 16 Sep external review set — S13 to S20				
S13		34 / 34	**CLOSED in v045**	Nothing — it was the blocker
S14		34 / 34	**CLOSED in code**	Live webhook verification
S15		0 / 42	Intelligence + eval	**PD-02 — build it, or reposition**
S16		0 / 29	Indic wedge, proven	**PD-02 + a consented call corpus**
S17		0 / 39	Live CRM depth	**CRM sandbox credentials**
S18		2 / 26	Commercial engine	**PD-01 — the price, and the model**
S19		0 / 32	Enterprise readiness	**PD-03 — SMB or enterprise first**
S20		0 / 12	Launch & proof	**Everything above, then strangers**

151 stories · 647 points · 377 complete (58%) — and the 42% that remains is mostly waiting on four decisions, not on engineering time.

Figure 4. The shape of the remaining work is unusual: four of the six incomplete sprints are blocked on a decision rather than on effort. S13 — the one the reviewer said blocked everything else — is closed.

7 · What is complete, and what is not — with the reason

Capability status at code v0.45.0. "Reachable" means a customer can invoke it through a route the typed client calls; it is machine-enforced by two standing gates.

Capability	Status	Why it is where it is
Install & tenancy	`Complete`	Workspace identity comes from Zoom, not the caller; a disagreeing hint is refused with an audit row. The takeover path found on 16 September is closed and pinned by two named regression tests.

Capability	Status	Why it is where it is
Sessions & access control	`Complete`	Real Zoom user and role, sixty-minute life, revocable individually or per workspace, delivered in an HttpOnly cookie. Owner/admin/member matrix with every decision — including denials — audit-logged.
HTTP hardening	`Complete`	CSP that admits the Zoom iframe, explicit CORS allowlist, 256 KB body cap, token-bucket limits per IP, per account and for the operator surface. Written without dependencies so it cannot drift with a transitive upgrade.
Durability	`Complete`	Nine PostgreSQL stores, each run through one contract suite twice — once in memory, once against a live database that CI refuses to skip. Tokens encrypted at rest; a purge is a real `DELETE`.
F1 Live notes	`Complete`	Durable since v0.45.0. It was the least durable thing in the product and the only thing a human typed by hand — a deploy during business hours used to discard every in-flight session.
F3 CRM writeback engine	`Complete`	Field mapping with per-field overwrite policy, a queue that survives a crash, retry with jitter, an audit row per write, and a human review step before anything is sent. This is the defensible part of the product.
Web panel	`Built, unverified`	Every panel now reads and writes through the API — it was a mock until v0.45.0. It has still never rendered inside the Zoom client; jsdom cannot judge colour contrast or screen-reader behaviour in a webview. *Needs a live install.*
F2 Action extraction	`Built, thin`	A five-phrase substring matcher. It works, it is honest, and it is worse than the free summariser Zoom now bundles. Whether it becomes a model or stays a rules engine is **decision PD-02**.
Billing	`Built, no money`	Trials, plans, proration, seat prompts, cancellation and entitlement enforcement all work. No payment processor exists, so no money has ever moved. *Needs PD-01 then ST-137.*
F4 Deal risk	`Held`	Thirteen hardcoded English keywords with no confidence score, unable to fire on the Hindi and Tamil calls the product is positioned for. Shipping it badly is worse than not shipping it — **decision PD-04**: rebuild inside real extraction, or cut it from the product and the pricing table.
F5 Indic pack	`Not built`	There is a word-error-rate ruler and nothing to measure with it: no speech recognition exists anywhere in the codebase. This is simultaneously the most defensible claim MeetSync could make and the least built thing in it. **PD-02**, then a consented corpus of real calls.
Intelligence (LLM/ASR)	`Not built`	No model, no inference, no embeddings — the review searched fifty-nine files and found the word "speech" inside one comment. The listing copy promising transcription is held behind a banner that the build gate enforces, so it cannot be submitted over code that does not back it.
Live CRM connection	`Not built`	Three sandbox adapters, zero live OAuth, zero real writes. *Needs HubSpot / Salesforce / Zoho sandbox credentials* — the one item here blocked purely on access rather than on a decision.
Data residency	`Not enforced`	The region setting is a label that is validated at boot and then only echoed. Rather than leave the claim standing, v0.45.0 removed it: `/trust` now reports `regionEnforced: false` and the page lists residency under "Not yet".
SSO · SOC 2 · pen test	`Not built`	An enterprise security questionnaire stops at question one. SOC 2 Type II is a funded programme — roughly $35K–$120K over six to eighteen months — not a sprint. Whether it starts now is **decision PD-03**.
Demand evidence	`None`	**Zero installs. Zero paying customers. Zero users outside the build.** 712 passing tests say the code does what it claims; they say nothing about whether anyone wants it. Three falsifiable demand tests are specified and unrun — **PD-06**.

> **The one-sentence version.** MeetSync has a platform most funded startups would envy wrapped around a feature set that is mostly keyword matching, and it has never met a customer.
> Everything an engineer can fix alone has been fixed; what remains needs four decisions, one set of credentials, and ten strangers willing to pay.

---

8 · Evidence behind the colouring

Claim	How it is enforced
"Built and tested"	712 tests across 40 suites; 100% statements, branches, functions and lines; zero coverage pragmas; TypeScript strict. CI fails below any of these.

Claim	How it is enforced
"Customer-reachable"	Two standing gates. Capability→caller fails the build when a capability has no caller; route→client fails it when a server route has no client method and no reasoned exemption.
"The trust page is true"	Document→code gate: every machine-checkable claim on the trust page is asserted against the running configuration, and a list of unbacked terms fails the build if they appear.
"Durable"	One contract suite per store, executed twice — in memory and against a live PostgreSQL 16 that CI provisions and refuses to skip.
"Never verified live"	Stated, not hidden: no Zoom account has ever installed this app, no CRM has ever received a write, no load test has run, no human has used the panel.

Sources: code v0.45.0 (`src/`, `web/`, `test/`, `docs/`), sprint tracker v040, Perplexity Review V001 of 16 September 2026.
Companion workbook: version detail, pending versions, step-by-step execution and manual test cases.
